

CAROLINA BAYS PARKWAY (SC 31)/ SC 707

PRESENTATION TO HORRY COUNTY COUNCIL
JUNE 18, 2013



Carolina Bays Parkway (SC 31) Extension/SC 707 Widening



Existing SC 707



Ending of Carolina Bays Parkway at SC 544


Carolina Bays Parkway (SC 31) Extension/SC 707 Widening

Project Description

Carolina Bays Parkway

Extension from current terminus at SC 544 to SC 707, a distance of approximately 3.8 miles. The proposed project is a new location, multilane freeway facility with a grassed median that will include a bridge over the Atlantic Intracoastal Waterway, a partial interchange at SC 544 and a full interchange at SC 707.

SCDOT is providing program and project management services through a 3-party intergovernmental agreement (IGA), between Horry County, the State Transportation Infrastructure Bank, and SCDOT signed on June 20, 2007

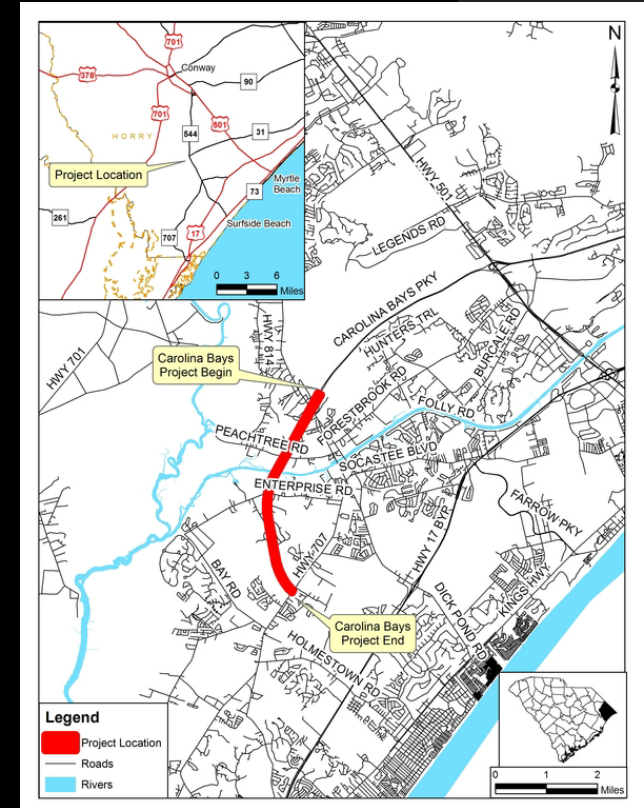

Carolina Bays Parkway (SC 31) Extension/SC 707 Widening

Carolina Bays Parkway



Early Clearing and Grubbing- Spring 2011



Early Clearing and Grubbing- Spring 2013


Carolina Bays Parkway (SC 31) Extension/SC 707 Widening

Project Description

SC 707 Widening

Widening from a 2-lane shoulder section to a 5-lane curb and gutter facility with sidewalks from just south of Enterprise Road (S-26-926) in Horry County to US Route 17 in Georgetown County, a distance of approximately 9.2 miles.

SCDOT is providing program and project management services through a 2-party intergovernmental agreement (IGA), between Horry County and SCDOT signed on June 22, 2007

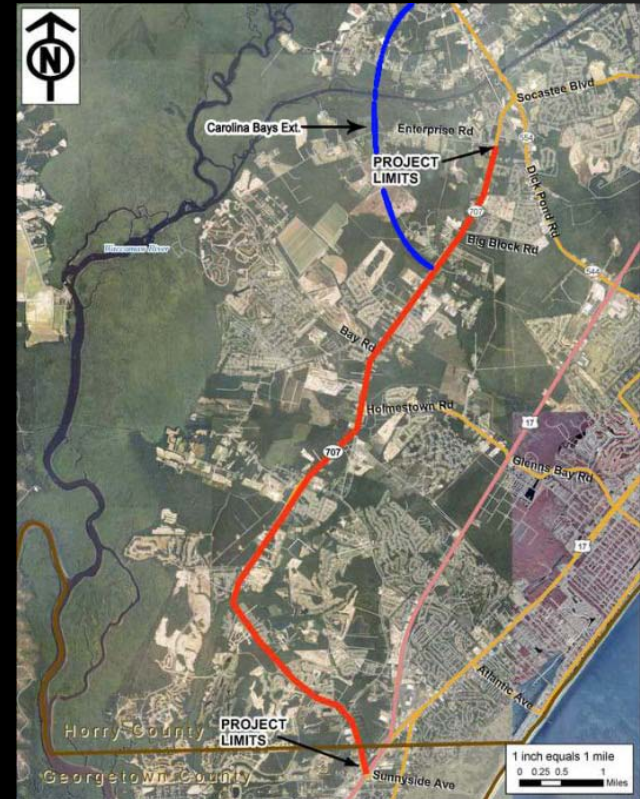

Carolina Bays Parkway (SC 31) Extension/SC 707 Widening

Status as of June 2013

Carolina Bays Parkway

- Preliminary Engineering complete
- Right of Way Acquisition complete
- May 24, 2013: A combined Carolina Bays Parkway/ SC 707 permit was approved by the US Army Corps of Engineers

SC 707 Widening

- Preliminary Engineering Complete
- Right of Way acquisition 95% complete
- May 24, 2013: A combined Carolina Bays Parkway/ SC 707 permit was approved by the US Army Corps of Engineers

Carolina Bays Parkway (SC 31) Extension/SC 707 Widening

Funding

Carolina Bays Parkway

- \$225M in State Transportation Infrastructure Bank (SIB) funds
- \$10M in American Recovery and Reinvestment Act (ARRA) funds
- \$2.4M in Earmark funds

SC 707 Widening

- \$100M to \$105M in Horry County local option sales tax funds

Carolina Bays Parkway (SC 31) Extension/SC 707 Widening

Delay Costs

Carolina Bays Parkway

- Approximately \$15M due to construction cost escalation
- Approximately \$640,000 in additional engineering fees

SC 707 Widening

- Approximately \$5.4M due to construction cost escalation

Carolina Bays Parkway (SC 31) Extension/SC 707 Widening

Schedule

Carolina Bays Parkway

- Letting in October 2013 (60-day ad with advertisement in August 2013)
- Notice to proceed in December 2013
- Project completion in Spring 2017

SC 707 Widening

- Letting of advanced clearing and grubbing project for utility relocations and SC 707/ Big Block Road interim intersection project in August 2013
- Completion of advanced clearing and grubbing project in Spring 2014
- Completion of SC 707/ Big Block Road interim intersection project in Fall 2014
- Letting of main widening project in Spring 2014
- Completion of main widening project in Spring 2017

Carolina Bays Parkway (SC 31) Extension/SC 707 Widening

QUESTIONS
